

December 16nd, 2021

South Capitol Bridgebuilders,
1220 12th Street, SE
Suite 255
Washington, DC 20003

Attention: Chad Bordovsky
(cbordovsky@walshgroup.com)

Subject: Biweekly PM10 Particulate Air Monitoring Report
South Capitol Street Frederick Douglass Memorial Bridge Corridor Project

Mr. Bordovsky,

Soil and Land Use Technology, Inc., (SaLUT) is pleased to provide perimeter air monitoring program for South Capitol Bridgebuilders and District Department of Transportation (DDOT). The intent of the program is to quickly alert the Project construction team to rising dust levels for swift resolution by the team in order to minimize dust.

Scope of Work

As per project requirements provided, SaLUT has mounted five solar powered aerosol meters (DustTrack Environmental 8540) around the perimeter of the project site mention above. See *Image 1- Location of air monitoring devices*. These devices provide field measurements of particulate matter as PM10 in ambient air. It provides real time analyses of particle matter at 10 μ m in diameter (PM10).

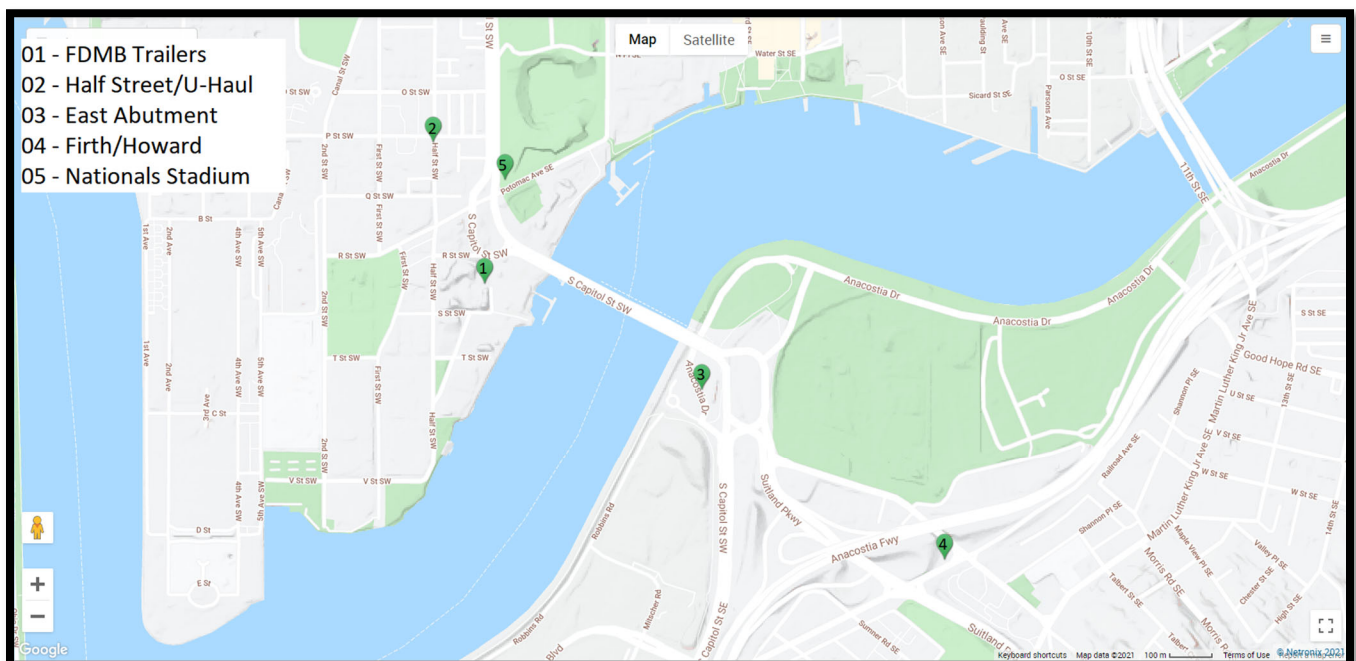


Image 1- Locations of air monitoring devices.

PM10 concentrations will be measured on a continuous basis at each station and will be reported as rolling 15 minute averages. An alert provides notification if a monitor is measuring concentrations equal to or greater than the 100 ug/m³. Responsible project personnel will be immediately notified via SMS and email notification to assess, validate, and then address the project-related air quality issue with additional dust control measures if/as needed in a timely fashion.

The instrument monitoring results are reviewed by the site air monitoring professional to ensure the rolling 15-minute average PM10 concentrations at the site are less than the AL. Please see the attached results from the period of November 21th to December 4th.

Conclusion

From November 21th to December 4th the alerts were not triggered. During this time period the project site was within compliance with national ambient air quality standards DC regulations.

We appreciate the opportunity to provide air monitoring services for SCB. Should you have any questions concerning this report, please do not hesitate to contact us at (240) 645-6764.

Sincerely,



Chamal Hettigama

Civil Engineer


Soil and Land Use Technology Inc. (SaLUT)

Attachments:

Attachment A: *Dust Levels Recorded by Instruments*

Attachment A – Dust levels recorded by the instruments
11/21/2021-12/04/2021


11/21/2021 12:43:00 – 12/04/2021 15:43:00
 (GMT-05:00) Eastern Time (US & Canada)

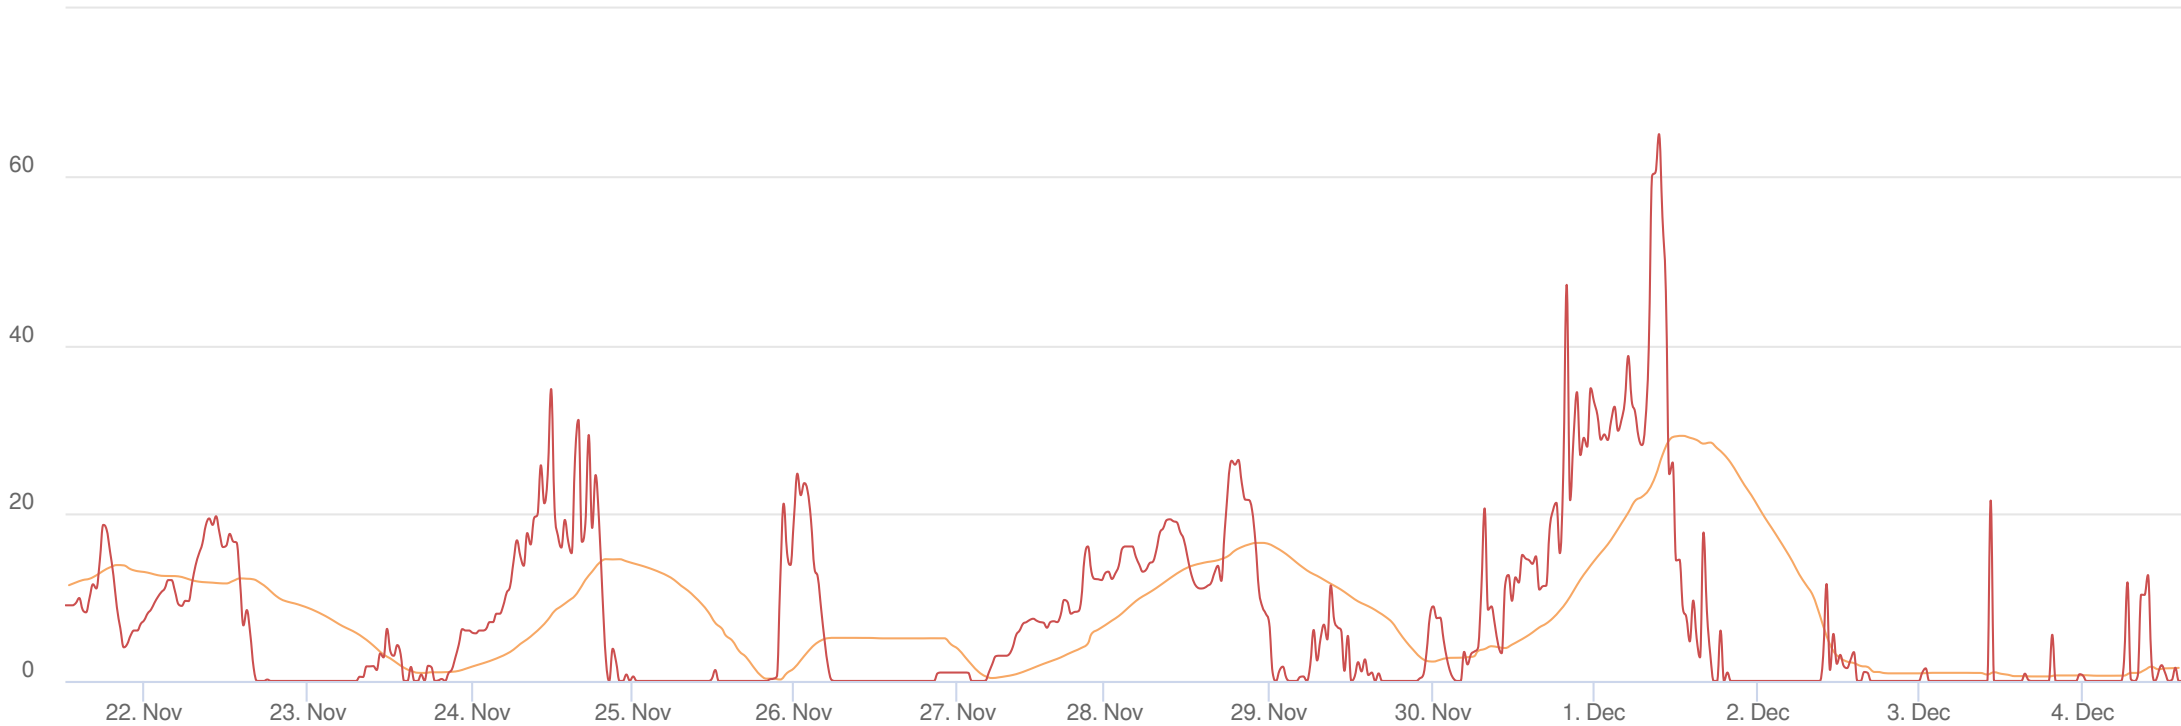

Mass Conc. Total $\mu\text{g}/\text{m}^3$ AVG 24hr			Mass Conc. Total $\mu\text{g}/\text{m}^3$ AVG 15m		
$\mu\text{g}/\text{m}^3$			$\mu\text{g}/\text{m}^3$		
DustTrak-8540			DustTrak-8540		
RS232(A)			RS232(A)		
MIN	AVG	MAX	MIN	AVG	MAX
0.1737	7.9809	29.164	0	7	81

Name 01 - FDMB Trailers
S/N 0B115512
Description S Capitol St (FDMB Trailers)
Location 1648 S Capitol St SE, Washington, DC 20003, USA

11/21/2021 12:47:00 – 12/04/2021 15:47:00
(GMT-05:00) Eastern Time (US & Canada)

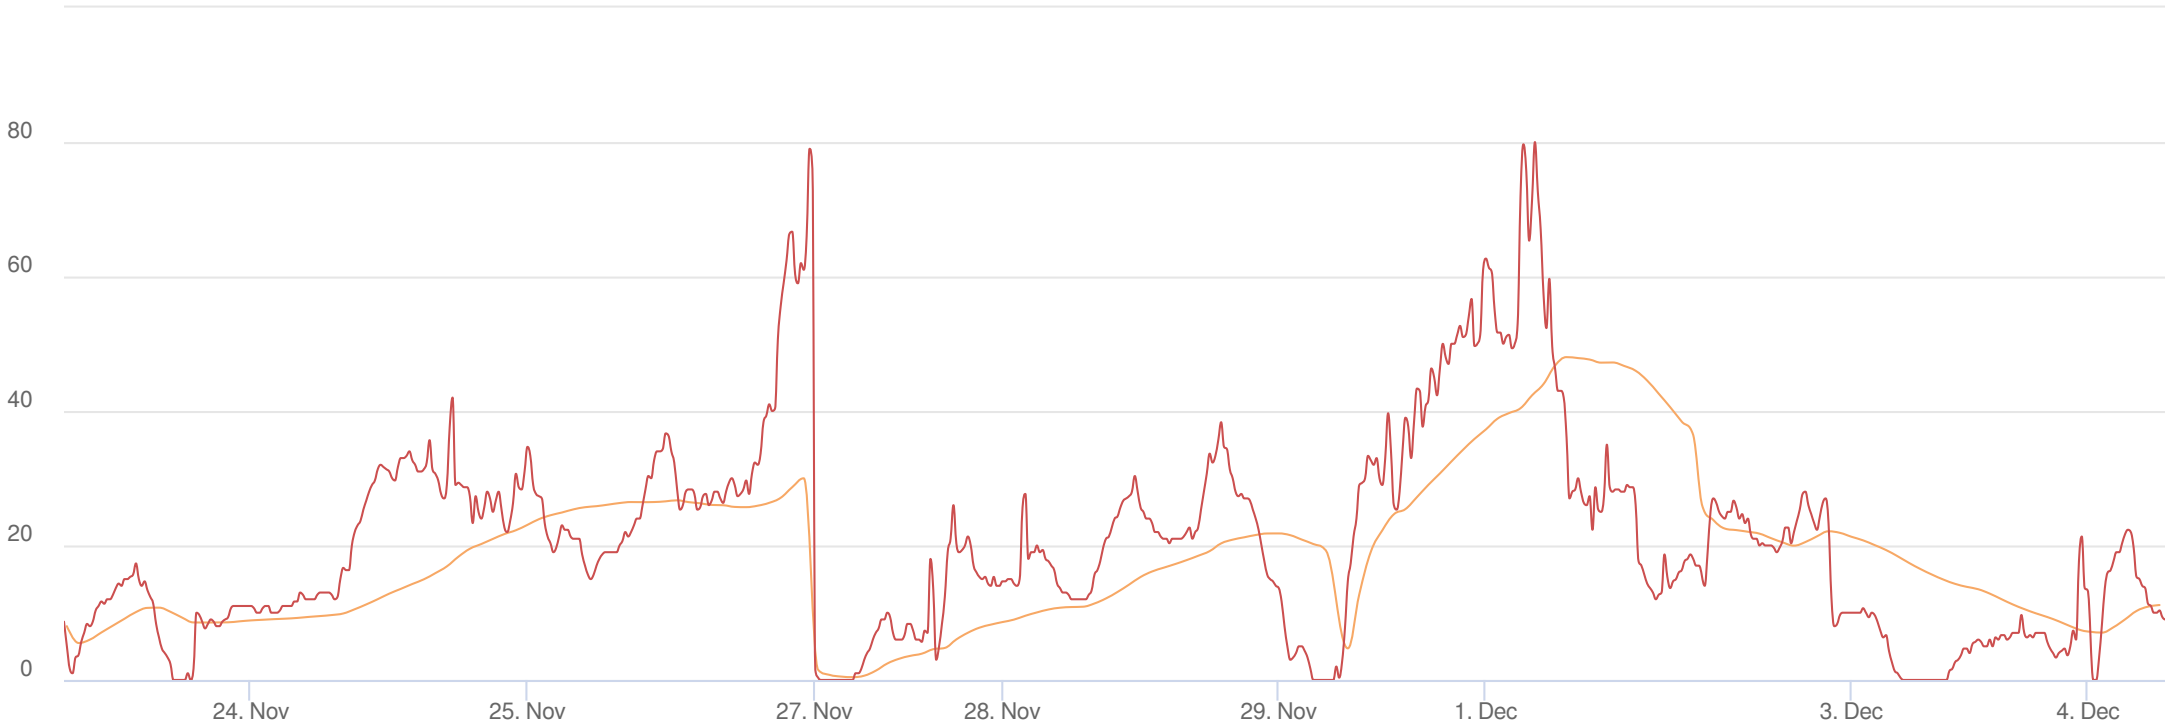

Mass Conc. Total $\mu\text{g}/\text{m}^3$ AVG 24hr $\mu\text{g}/\text{m}^3$ DustTrak-8540 RS232(A)			Mass Conc. Total $\mu\text{g}/\text{m}^3$ AVG 15m $\mu\text{g}/\text{m}^3$ DustTrak-8540 RS232(A)		
MIN	AVG	MAX	MIN	AVG	MAX
0.41667	18.697	48.013	0	21	82

Name 02 - Half Street/U-Haul
S/N 0B392918
Description Half St & P St
Location 1427 Carrollsburg Pl
SW, Washington, DC
20024, USA


11/21/2021 12:48:00 – 12/04/2021 15:48:00
(GMT-05:00) Eastern Time (US & Canada)



Mass Conc. Total $\mu\text{g}/\text{m}^3$ AVG 24hr			Mass Conc. Total $\mu\text{g}/\text{m}^3$ AVG 15m		
$\mu\text{g}/\text{m}^3$			$\mu\text{g}/\text{m}^3$		
DustTrak-8540			DustTrak-8540		
RS232(A)			RS232(A)		
MIN	AVG	MAX	MIN	AVG	MAX
0.42059	18.538	63.111	0	16	86

Name 03 - East Abutment
S/N 0B392923
Description Anacostia Dr (Yard)
Location VX8W+RC Washington, DC, USA


11/21/2021 12:49:00 – 12/04/2021 15:49:00
 (GMT-05:00) Eastern Time (US & Canada)

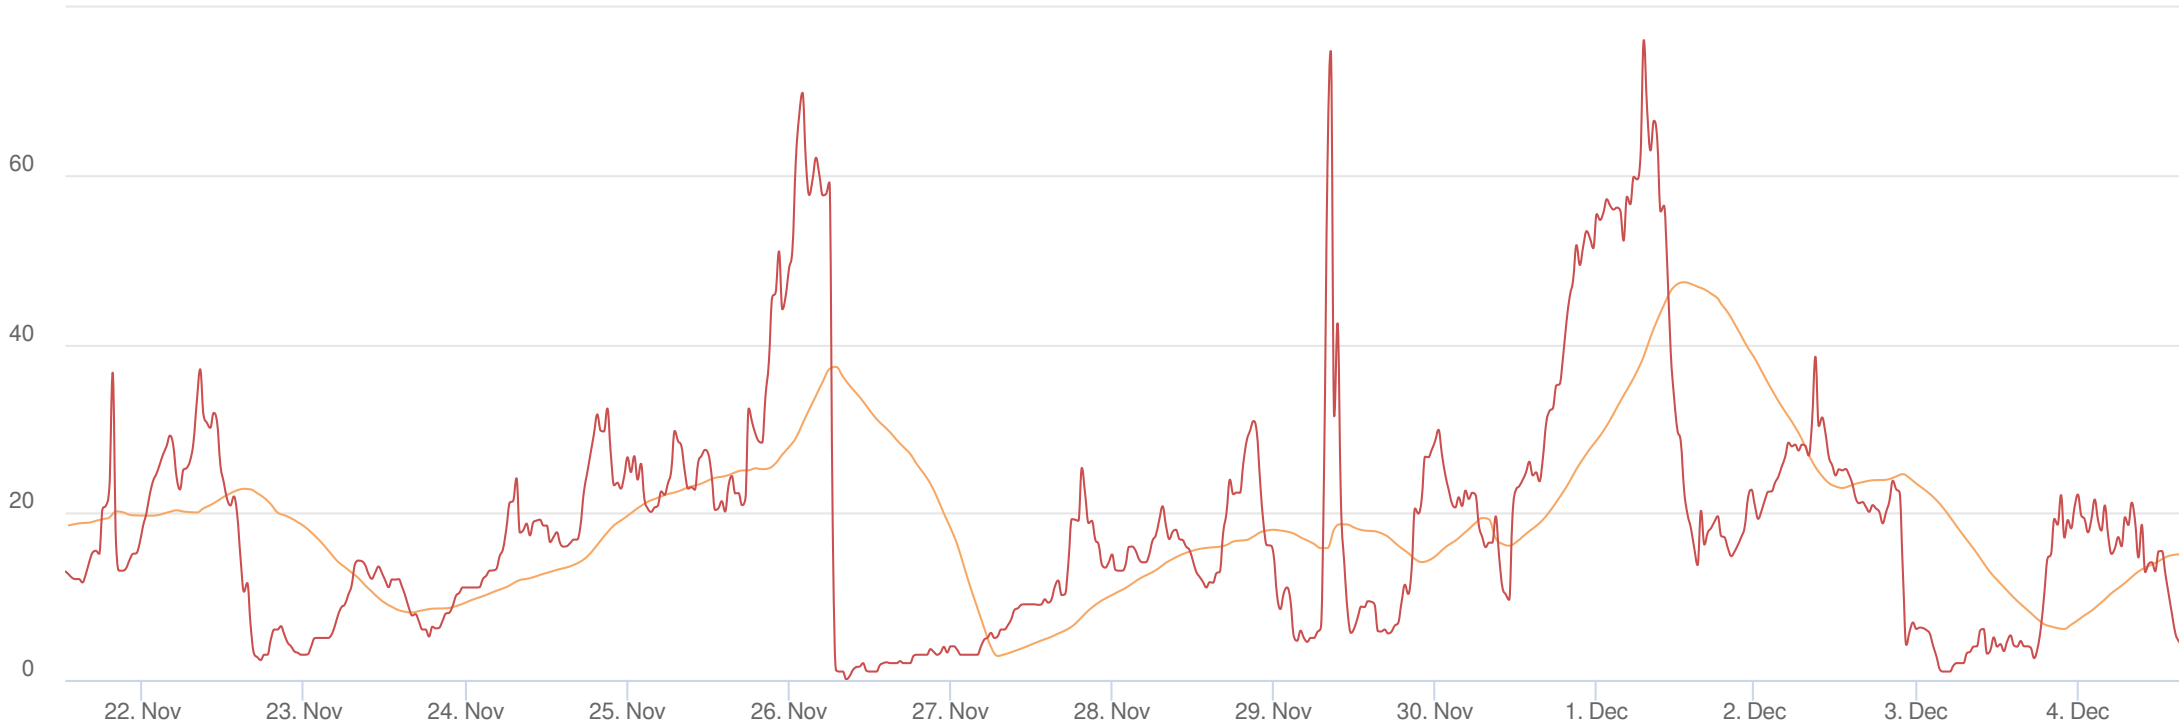

Mass Conc. Total $\mu\text{g}/\text{m}^3$ AVG 24hr			Mass Conc. Total $\mu\text{g}/\text{m}^3$ AVG 15m		
$\mu\text{g}/\text{m}^3$			$\mu\text{g}/\text{m}^3$		
DustTrak-8540			DustTrak-8540		
RS232(A)			RS232(A)		
MIN	AVG	MAX	MIN	AVG	MAX
2.8583	19.325	47.323	0	19	96

Name 04 - Firth/Howard
S/N 0B282540
Description Howard Rd & Firth
 Sterling Ave
Location Anacostia, 1101
 Howard Rd SE,
 Washington, DC 20020,
 USA

11/21/2021 12:50:00 – 12/04/2021 15:50:00
 (GMT-05:00) Eastern Time (US & Canada)

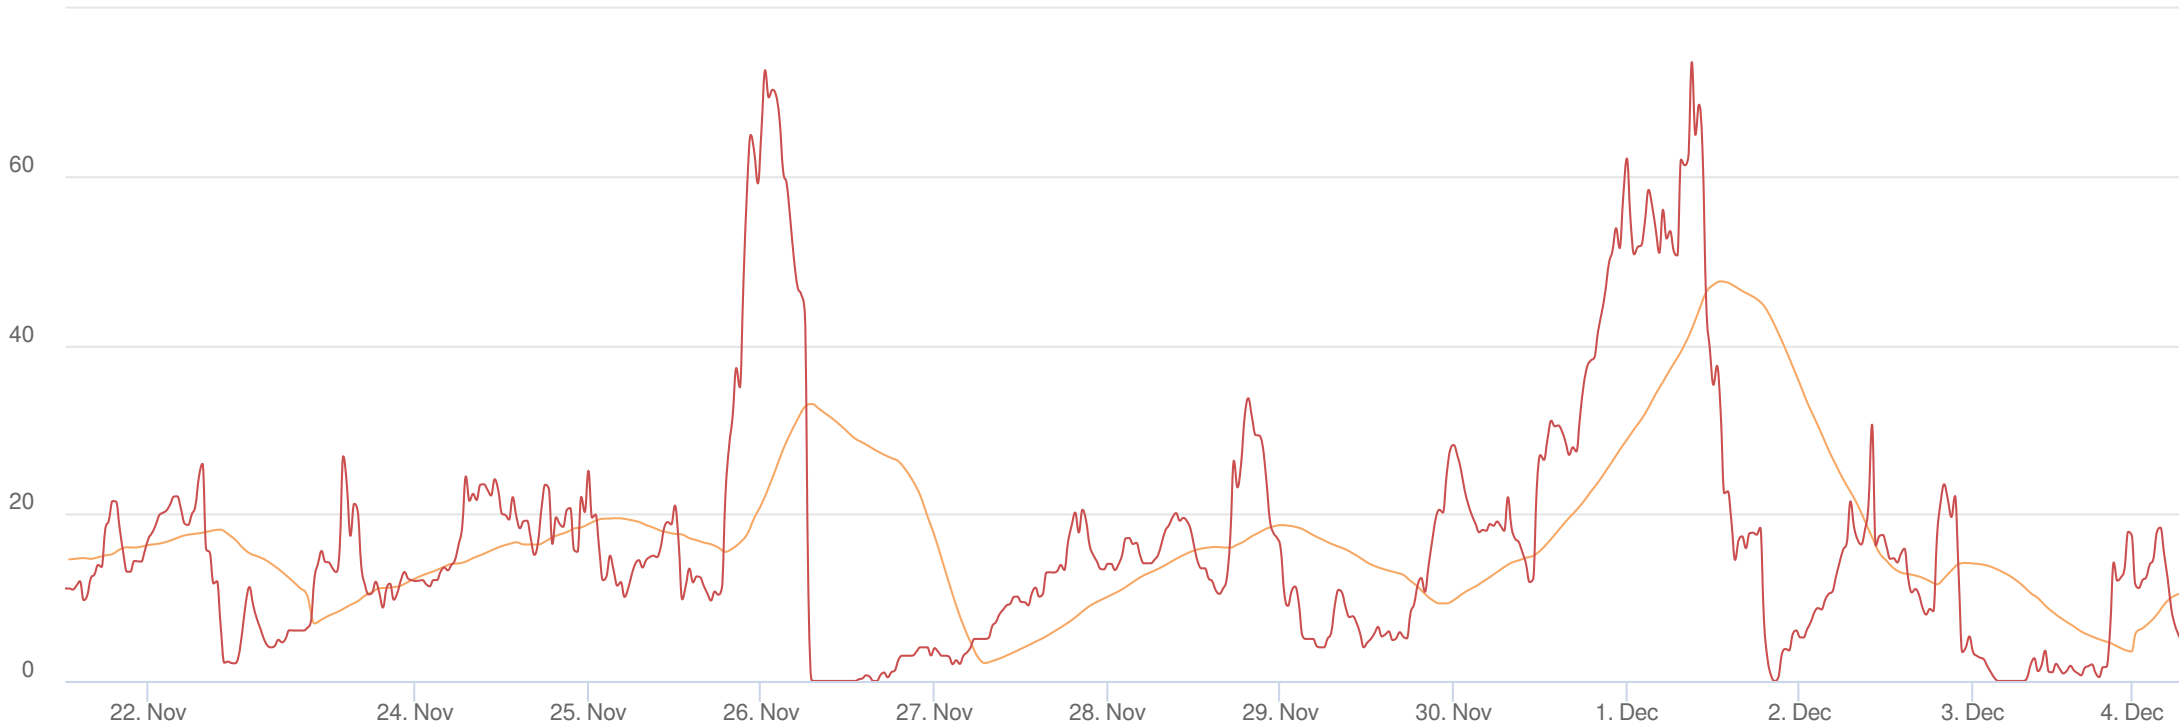

Mass Conc. Total µg/m³ AVG 24hr µg/m³ DustTrak-8540 RS232(A)			Mass Conc. Total µg/m³ AVG 15m µg/m³ DustTrak-8540 RS232(A)		
MIN	AVG	MAX	MIN	AVG	MAX
2.1374	17.1995	47.539	0	16	85

Name 05 - Nationals Stadium
S/N 0B350099
Description S Capitol St & Potomac Ave
Location 2872 Potomac Ave SE, Washington, DC 20003, USA
