

November 2<sup>nd</sup>, 2021

South Capitol Bridgebuilders,  
1220 12th Street, SE  
Suite 255  
Washington, DC 20003  
Attention: Chad Bordovsky  
([cbordovsky@walshgroup.com](mailto:cbordovsky@walshgroup.com))


Subject: Biweekly PM10 Particulate in Air Monitoring Report  
South Capitol Street Frederick Douglass Memorial Bridge Corridor Project

Mr. Bordovsky,

Soil and Land Use Technology, Inc., (SaLUT) is pleased to provide perimeter air monitoring program for South Capitol Bridgebuilders and District Department of Transportation (DDOT). The intent of the program is to quickly alert the Project construction team to rising dust levels for swift resolution by the team in order to minimize dust.

### Scope of Work

As per project requirements provided, SaLUT has mounted five solar powered aerosol meters (DustTrack Environmental 8540) around the perimeter of the project site mention above. See *Image 1- Location of air monitoring devices*. These devices provide field measurements of particulate matter as PM10 in ambient air. It provides real time analyses of particle matter at 10 $\mu$ m in diameter (PM10).

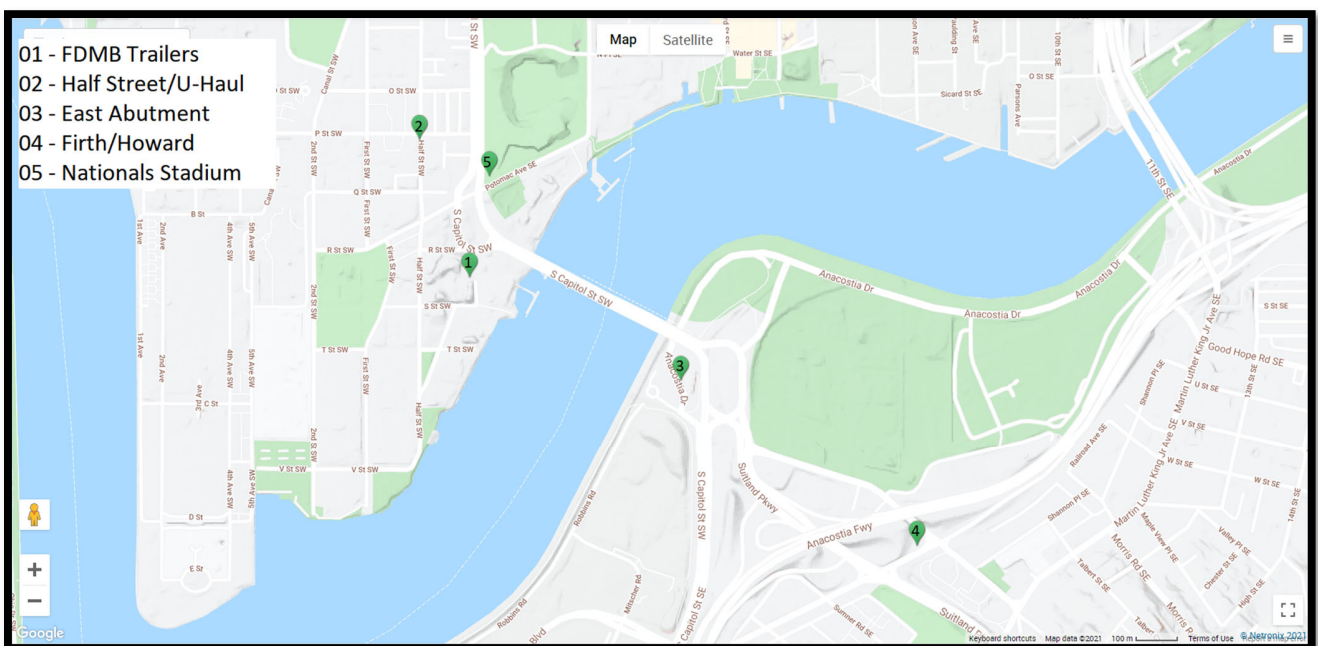

**Image 1- Locations of air monitoring devices.**

PM10 concentrations will be measured on a continuous basis at each station and will be reported as rolling 15 minute averages. An alert provides notification if a monitor is measuring concentrations equal to or greater than the 100 ug/m<sup>3</sup>. Responsible project personnel will be immediately notified via SMS and email notification to assess, validate, and then address the project-related air quality issue with additional dust control measures if/as needed in a timely fashion. The responsible personnel will identify the source of the deficiency and the appropriate means to mitigate dust emissions from the project site.

The instrument monitoring results are reviewed by the site air monitoring professional to ensure the rolling 15-minute average PM10 concentrations at the site are less than the AL. Please see the attached results from the period of September 26<sup>th</sup> to October 9<sup>th</sup>.

### **Conclusion**

From September 26<sup>th</sup> – October 9<sup>th</sup> the alerts were triggered three time and each time corrective actions were taken to mitigate dust emissions from the project within under 10 minutes. During this time period the project site was within compliance with national ambient air quality standards DC regulations.

We appreciate the opportunity to provide air monitoring services for SCB. Should you have any questions concerning this report, please do not hesitate to contact us at (240) 645-6764.

Sincerely,



**Chamal Hettigama**

Civil Engineer

Soil and Land Use Technology Inc. (SaLUT)

### **Attachments:**

**Attachment A:**            *Dust Levels Recorded by Instruments*




1818 New York Ave. NE, Suite 231  
Washington, DC 20002

Soil and Land Use Technology, Inc.  
Telephone: (301) 595-3783  
[www.salutinc.com](http://www.salutinc.com)

**Attachment A – Dust levels recorded by the instruments**  
**09/26/2021-10/09/2021**

09/26/2021 4:34:00 – 10/09/2021 7:34:00  
(GMT-05:00) Eastern Time (US & Canada)

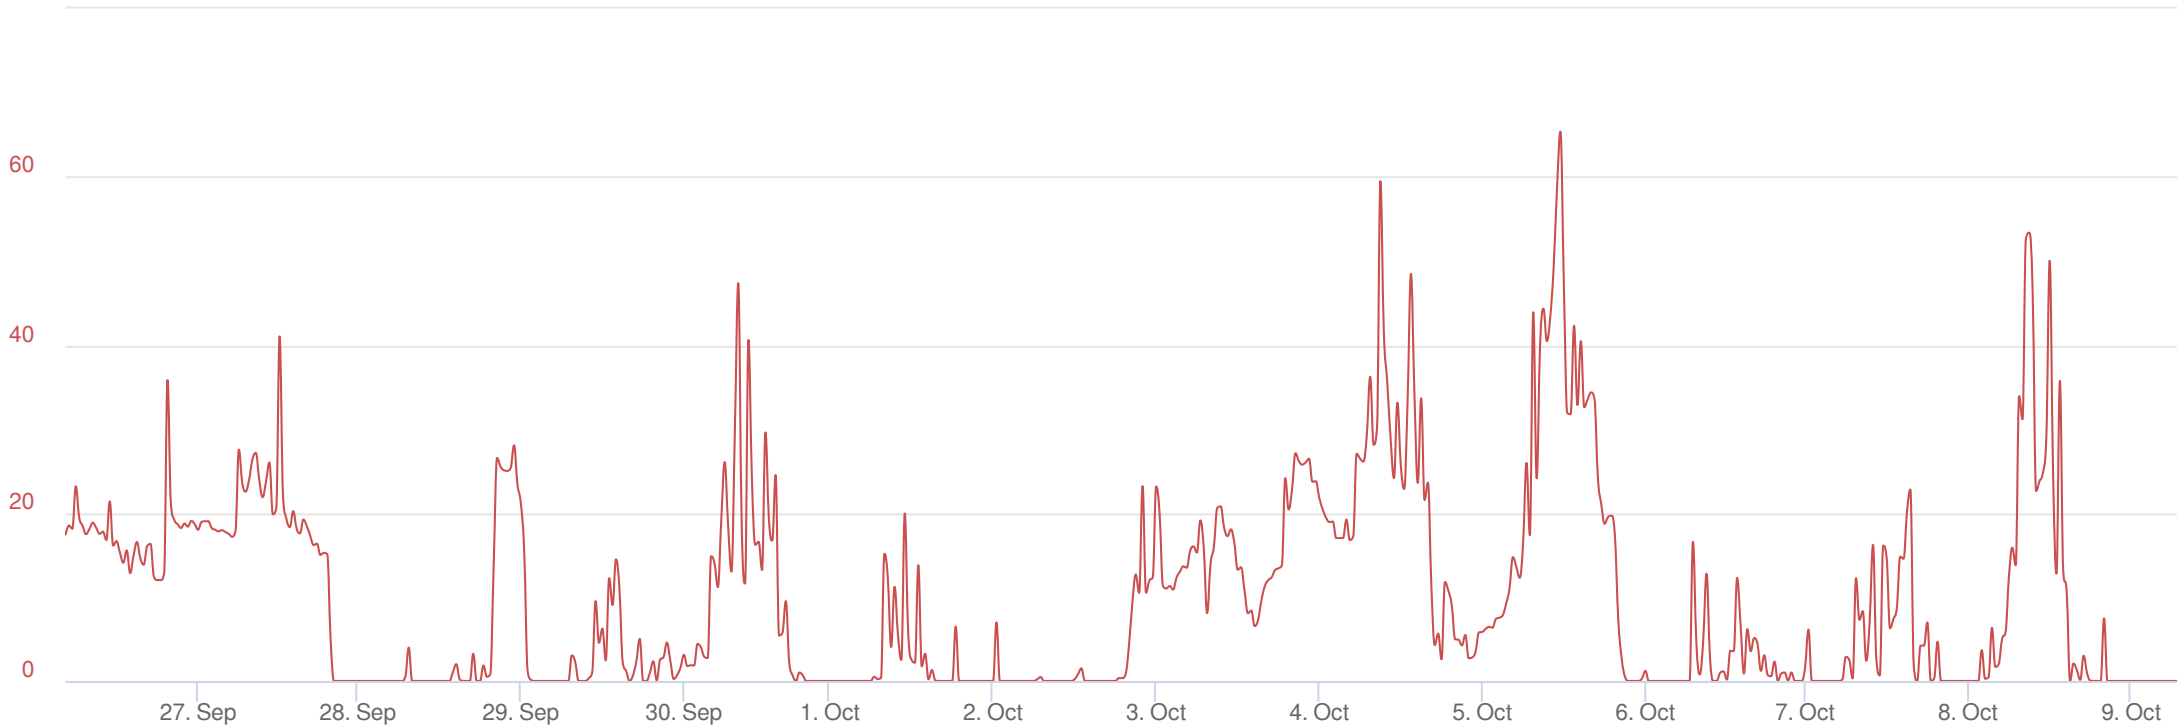

**Mass Conc. Total  $\mu\text{g}/\text{m}^3$  AVG 15m**

$\mu\text{g}/\text{m}^3$

DustTrak-8540

RS232(A)

MIN

0

AVG

10

MAX

111

**Name** 01 - FDMB Trailers  
**S/N** 0B115512  
**Description** S Capitol St (FDMB Trailers)  
**Location** 1724 S Capitol St SE, Washington, DC 20003, USA

09/26/2021 4:38:00 – 10/09/2021 7:38:00  
(GMT-05:00) Eastern Time (US & Canada)



**Mass Conc. Total  $\mu\text{g}/\text{m}^3$  AVG 15m**

$\mu\text{g}/\text{m}^3$

DustTrak-8540

RS232(A)

MIN

0

AVG

28

MAX

80

**Name** 02 - Half Street/U-Haul  
**S/N** 0B392918  
**Description** Half St & P St  
**Location** 50 P St SW, Washington, DC 20024, USA

09/26/2021 4:39:00 – 10/09/2021 7:39:00  
(GMT-05:00) Eastern Time (US & Canada)



**Mass Conc. Total µg/m³ AVG 15m**

µg/m³

DustTrak-8540

RS232(A)

MIN

0

AVG

26

MAX

96

**Name** 03 - East Abutment  
**S/N** 0B392923  
**Description** Anacostia Dr (Yard)  
**Location** VX8W+CQ Washington,  
DC, USA

09/26/2021 4:41:00 – 10/09/2021 7:41:00  
(GMT-05:00) Eastern Time (US & Canada)



**Mass Conc. Total µg/m³ AVG 15m**

µg/m³

DustTrak-8540

RS232(A)

MIN

0

AVG

12

MAX

62

**Name** 04 - Firth/Howard

**S/N** 0B282540

**Description** Howard Rd & Firth  
Sterling Ave

**Location** Anacostia, 1101  
Howard Rd SE,  
Washington, DC 20020,  
USA

09/26/2021 4:42:00 – 10/09/2021 7:42:00  
(GMT-05:00) Eastern Time (US & Canada)



**Mass Conc. Total  $\mu\text{g}/\text{m}^3$  AVG 15m**

$\mu\text{g}/\text{m}^3$

DustTrak-8540

RS232(A)

MIN

0

AVG

5

MAX

61

**Name** 05 - Nationals Stadium  
**S/N** 0B350099  
**Description** S Capitol St & Potomac Ave  
**Location** 2872 Potomac Ave SE,  
Washington, DC 20003,  
USA
